


EQUIPMENT SCHEDULE			
TAG	DESCRIPTION	PART NUMBER	NOTES
1	PV DC or AC MODULE		
2	DC/AC INVERTER (MICRO)		
3	J-BOX (IF USED)		
4	PV ARRAY		
5	AC COMB. PANEL (IF USED)		
6	GEN METER (IF USED)		
7	AC DISCONNECT (IF USED)		
8	SERVICE PANEL		

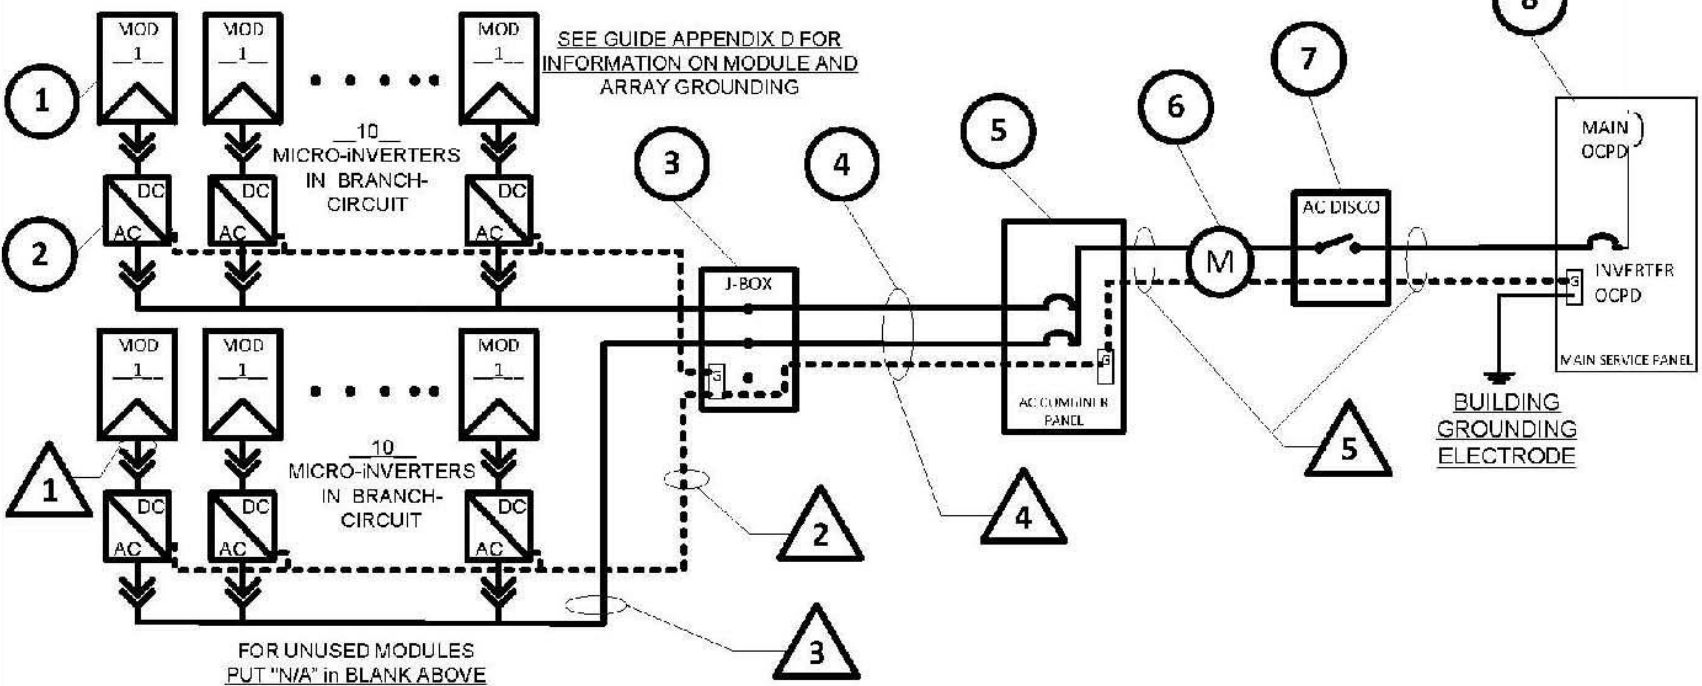

CONDUIT AND CONDUCTOR SCHEDULE					
TAG	DESCRIPTION OR CONDUCTOR TYPE	COND. GAUGE	NUMBER OF CONDUCTORS	CONDUIT TYPE	CONDUIT SIZE
1	USE-2 <input type="checkbox"/> or PV WIRE <input type="checkbox"/>			N/A	N/A
2	GEC <input checked="" type="checkbox"/> EGC <input checked="" type="checkbox"/> X ALL THAT APPLY			N/A	N/A
3	EXTERIOR CABLE LISTED W/ INV.				
4	THWN-2 <input checked="" type="checkbox"/> or XHHW-2 <input type="checkbox"/> or RHW-2 <input type="checkbox"/> GEC <input checked="" type="checkbox"/> EGC <input checked="" type="checkbox"/> X ALL THAT APPLY				
	NO DC GEC IF 690.35 SYSTEM				
5	THWN-2 <input checked="" type="checkbox"/> or XHHW-2 <input type="checkbox"/> or RHW-2 <input type="checkbox"/> GEC <input checked="" type="checkbox"/> EGC <input checked="" type="checkbox"/> X ALL THAT APPLY				

Contractor Name,  
Address and Phone:

Drawn By:

Checked by:

**One-Line Standard Electrical Diagram  
for Micro-Inverter or AC Module PV Systems**

Site Name: \_\_\_\_\_

Site Address: \_\_\_\_\_

System AC Size: 4.0 KW

SIZE	FSCM NO	DWG NO	REV
		E1.1a	0
SCALE	NTS	Date:	SHEET
